

ON-SITE SERVICES LOCATION DIAGRAM

This form is to be completed by the Contractor and submitted to the Building Inspector at the time of the Service Inspection.

ADDRESS: _____ BP No.: _____

INSTALLER: _____ SIGNATURE: _____

BUSINESS LICENCE #: _____

PERIMETER DRAINS

- PERF. PVC – SIZE: _____
- BIG O – SIZE: _____
- WINDOW WELL DRAIN “TEED”
- STAIRWELL DRAIN 12”

HIGH POINT OF TILES X HP _____
FROM TOP OF CONCRETE.

INFILTRATION GALLERY

SUMP SIZE

- 24” (5'-0” MAX DEPTH)
- 30” (8'-0” MAX DEPTH)
- 36” C/W LADDER
(OVER 8'-0” DEEP)

WATER LINE


- 3/4”
- 1’
- POLYETHYLENE – CSA B137.1
- PEX B 137.5
- COPPER K ASTM B88
- PVC SCHEDULE 40 OR 80
SCA B137.3 –

DAMPROOFING

- DIMPLE MEMBRANE
(Certificate Attached)
- EMULSION

NOTE

1. SOLID PVC REQ'D UNDER DRIVEWAY
2. SOLID PVC REQUIFRED FROM PERIMETER DRAINS TO SUMP
3. WATER METER LOCATION TO BE INDICATED.
4. SANITARY LINE & I.C. LOCATION TO BE INDICATED

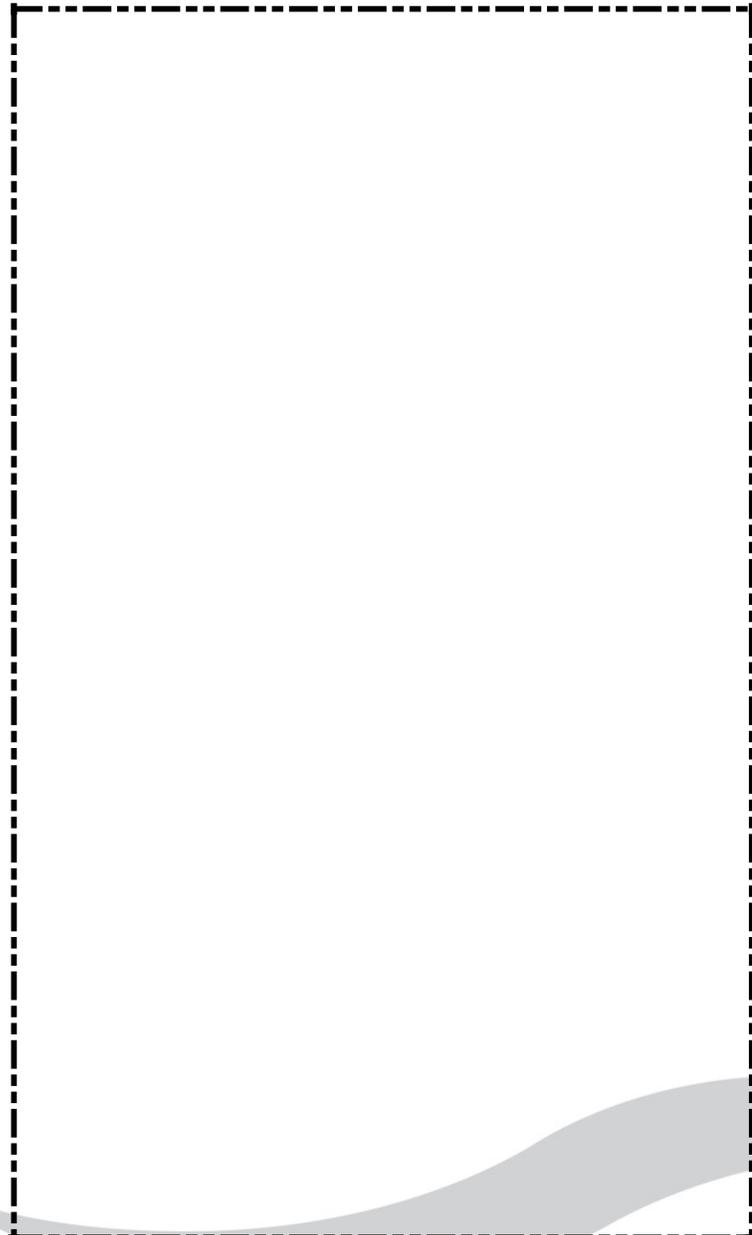

ADJOINING LOT PROPERTY LINE

STREET
